Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	15 October 2026
Team ID	SkillWallet — ServiceNow Project
Project Name	Automated Employee Onboarding & Offboarding System
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Roles & Security Setup	USN-1	As an admin, I can create the 4 groups (HR, IT, Facilities, Security) so role-based access is structured.	2	High	Uma Maheshwari
Sprint-1	Roles & Security Setup	USN-2	As an admin, I can assign roles (hr.manager, it.admin, facilities.staff, security.officer) to each group.	2	High	Uma Maheshwari
Sprint-1	Data Architecture	USN-3	As an admin, I can create the custom table u_employee_lifecycle with all required fields.	3	High	Uma Maheshwari
Sprint-1	Data Architecture	USN-4	As an admin, I can define choice values for Request Type (Onboarding / Offboarding) and Status (New / In Progress / Completed / Rejected).	2	High	Uma Maheshwari
Sprint-1	Data Architecture	USN-5	As an admin, I can configure reference fields (Department, Manager, Requested For) on the table.	2	Medium	Uma Maheshwari
Sprint-2	Catalog Item	USN-6	As an HR Manager, I can submit an onboarding request via the Service Portal catalog item.	3	High	Uma Maheshwari
Sprint-2	Catalog Item	USN-7	As an HR Manager, I can fill 13 catalog variables including Employee ID, Department, Manager, Joining Date.	3	High	Uma Maheshwari
Sprint-2	Catalog Item	USN-8	As an HR Manager, I can see only the relevant date field (Joining Date for Onboarding / Exit Date for Offboarding) based on Request Type.	2	High	Uma Maheshwari
Sprint-2	Catalog Item	USN-9	As an admin, I can enforce mandatory fields (Employee ID, Request Type, Department, Manager, Joining Date) to prevent incomplete submissions.	2	High	Uma Maheshwari
Sprint-2	Catalog UI Policies	USN-10	As an admin, I can create 4 UI policies to dynamically show/hide date fields.	2	Medium	Uma Maheshwari
Sprint-3	Automation Logic	USN-11	As a system, I can trigger the Flow Designer flow when the catalog item is submitted.	3	High	Uma Maheshwari
Sprint-3	Automation Logic	USN-12	As the flow, I can use "Get Catalog Variables" to retrieve submitted values.	2	High	Uma Maheshwari
Sprint-3	Automation Logic	USN-13	As the flow, I can create a lifecycle record with mapped variables and Status = New.	3	High	Uma Maheshwari
Sprint-3	Automation Logic	USN-14	As the flow, I can route a manager approval with all request details.	3	High	Uma Maheshwari
Sprint-3	Automation Logic	USN-15	As the flow, I can create 3 tasks on approval — IT, Facilities, Security — with correct assignment groups.	5	High	Uma Maheshwari

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-3	Automation Logic	USN-16	As the flow, I can wait for all 3 tasks to be Closed Complete before continuing.	3	High	Uma Maheshwari
Sprint-3	Automation Logic	USN-17	As the flow, I can update the lifecycle record Status = Completed and close the RITM.	3	High	Uma Maheshwari
Sprint-3	Automation Logic	USN-18	As the flow, I can send approval and completion email notifications.	2	High	Uma Maheshwari
Sprint-3	Automation Logic	USN-19	As the flow, I can handle the rejected path — log rejection, close RITM as Incomplete, send email.	3	Medium	Uma Maheshwari
Sprint-4	Access Control	USN-20	As an admin, I can elevate to security_admin and create ACLs (read/write/create/delete) on the lifecycle table.	3	High	Uma Maheshwari
Sprint-4	SLA Configuration	USN-21	As a Service Manager, I can attach an SLA (1-day target) to IT tasks assigned to IT – Account Provisioning group.	2	Medium	Uma Maheshwari
Sprint-4	Testing & Security	USN-22	As a QA, I can perform an end-to-end test (submit → approve → close tasks → verify completion).	3	High	Uma Maheshwari
Sprint-4	Testing & Security	USN-23	As a QA, I can verify the rejection path handles requests correctly.	2	Medium	Uma Maheshwari
Sprint-4	Documentation & Deployment	USN-24	As a project lead, I can document the solution (functional, technical, setup manual, demo).	5	High	Uma Maheshwari
Sprint-4	Documentation & Deployment	USN-25	As a project lead, I can record the demo video and prepare the final presentation.	3	High	Uma Maheshwari
			Total Story Points	**68**		

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	11	6 Days	01 Oct 2026	06 Oct 2026	11	06 Oct 2026
Sprint-2	12	6 Days	07 Oct 2026	12 Oct 2026	12	12 Oct 2026
Sprint-3	27	6 Days	13 Oct 2026	18 Oct 2026	27	18 Oct 2026
Sprint-4	18	6 Days	19 Oct 2026	24 Oct 2026	18	24 Oct 2026
Total	**68**	**24 Days**			**68**	

Velocity:

Velocity is the amount of work (in story points) a team completes in a single sprint, and is used to forecast future sprints. With a sprint duration of 6 days and a total of 68 story points delivered across 4 sprints, the team's average velocity is 68/4 = 17 story points per sprint. The average velocity (AV) per iteration unit (story points per day) is:


AV = velocity / sprint duration = 17 / 6 = 2.83 story points per day

Sprint	Story Points	Duration	Velocity (points/day)
Sprint-1	11	6 days	1.83
Sprint-2	12	6 days	2.00
Sprint-3	27	6 days	4.50
Sprint-4	18	6 days	3.00
Average	**17**	**6 days**	**2.83**

Burndown Chart:

A burn down chart is a graphical representation of work left to do versus time. It is often used in agile software development methodologies such as Scrum. However, burn down charts can be applied to any project containing measurable progress over time.

Day	Ideal Remaining	Actual Remaining
Day 0	27	27
Day 1	22.5	24
Day 2	18	18
Day 3	13.5	15
Day 4	9	8
Day 5	4.5	4
Day 6	0	0

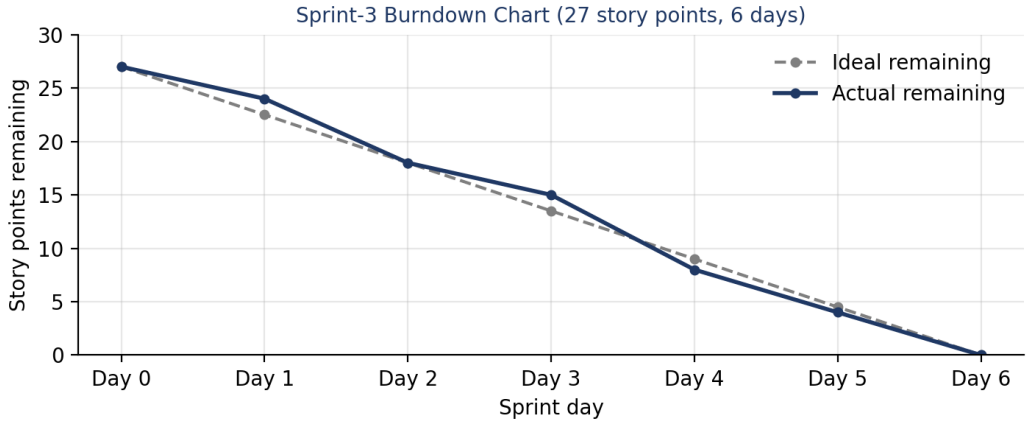

Interpretation: In Sprint-3 (27 story points, 6 days) the team tracked slightly behind the ideal line on Days 1–3 but caught up on Days 4–6, delivering all 27 story points by the end of the sprint.

Summary

Sprint	Focus Area	Stories	Points	Duration	Status
Sprint-1	Roles, Groups, Custom Table	5	11	6 days	Complete
Sprint-2	Catalog Item + UI Policies	5	12	6 days	Complete
Sprint-3	Flow Designer Automation	9	27	6 days	Complete
Sprint-4	ACLs, SLA, Testing, Docs	6	18	6 days	Complete
Total	—	**25**	**68**	**24 days**	

Team size: 1 (Uma Maheshwari) | Average velocity: 2.83 points/day | Average per sprint: 17 points | Completion rate: 100%

Reference:

https://www.atlassian.com/agile/project-management
https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software
https://www.atlassian.com/agile/tutorials/epics
https://www.atlassian.com/agile/tutorials/sprints
https://www.atlassian.com/agile/project-management/estimation
https://www.atlassian.com/agile/tutorials/burndown-charts
